CHƯƠNG 5. KẾT THÚC VÀ ĐÁNH GIÁ DỰ ÁN (3 LT)


1. Kết thúc dự án
2. Đánh giá dự án

1. Kết thúc dự án

Closing Processes

- Administrative Closure Procedure
  - Details all the activities, interactions, and related roles and responsibilities of the project team members and other stakeholders involved in executing the administrative closure procedures for the project
  - Should be included in the project control book
- Project closure:
  - Is executed to bring the project to successful completion
  - Is planned at the beginning of the project
  - Should be budgeted, and scheduled
  - Should involve the same group of people involved in project startup
  - Must be done because it provides a lasting impression on your customers and stakeholders

Design for Project Closure

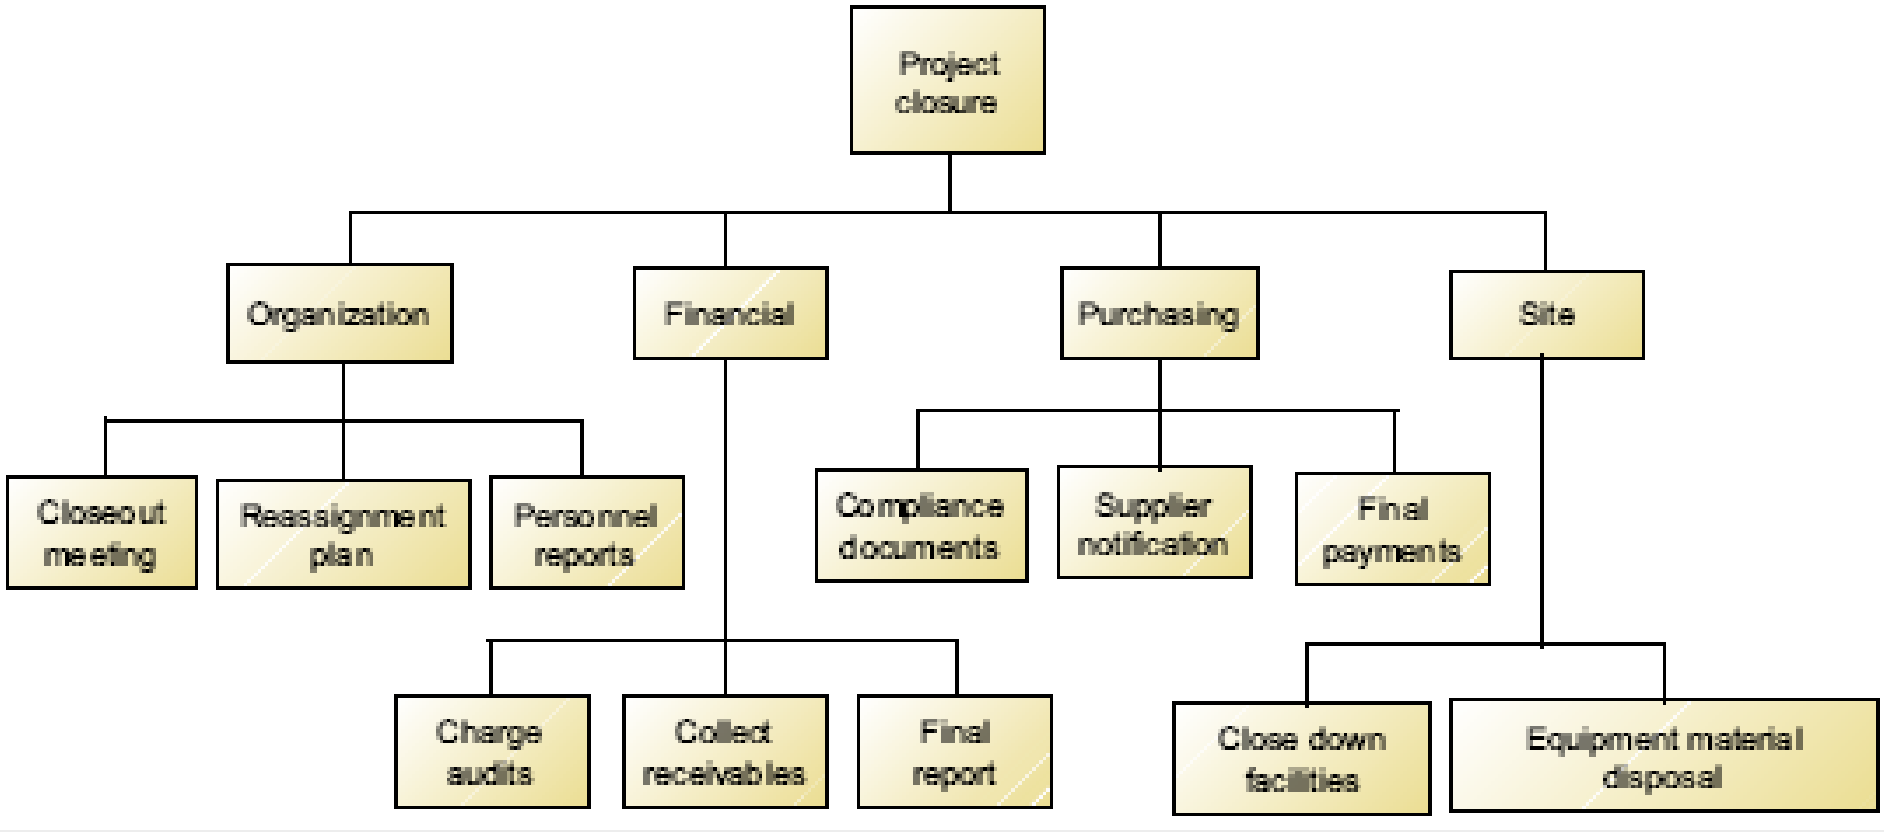

Project closure should be planned, budgeted, and scheduled

Project Closure Activities

- Project closure activities include:
  - Develop a transition plan
    - Deliver the solution to the client
  - Conduct administrative closure
    - Complete all documents associated with project measurement
    - Gather all information about the project and formalize project closure
  - Close client/sponsor activity
  - Close contracts
    - Complete and terminate all contracts
    - Resolve all open issues
  - Implement the closeout plan
  - Compiling and disseminating
  - Lessons Learned
  - Sign the completion documentation


Contract Closure Procedure

- Contract Closure Procedure - Includes all activities and interactions needed to settle and close any contract agreement established for the project, as well as define those related activities supporting the formal administrative closure of the project
- Contract closure procedure involves:
  - Product verification - Has all work been completed correctly and satisfactorily?
  - Administrative closure - Updating of contract records to reflect final results and archiving that information for future use

Contract terms and conditions might also prescribe specifications for closing the contract which would need to be made part of the procedure

Close Procurements

- The process of finalizing all activities across all of the Project Management Process Groups to formally complete the project or phase.

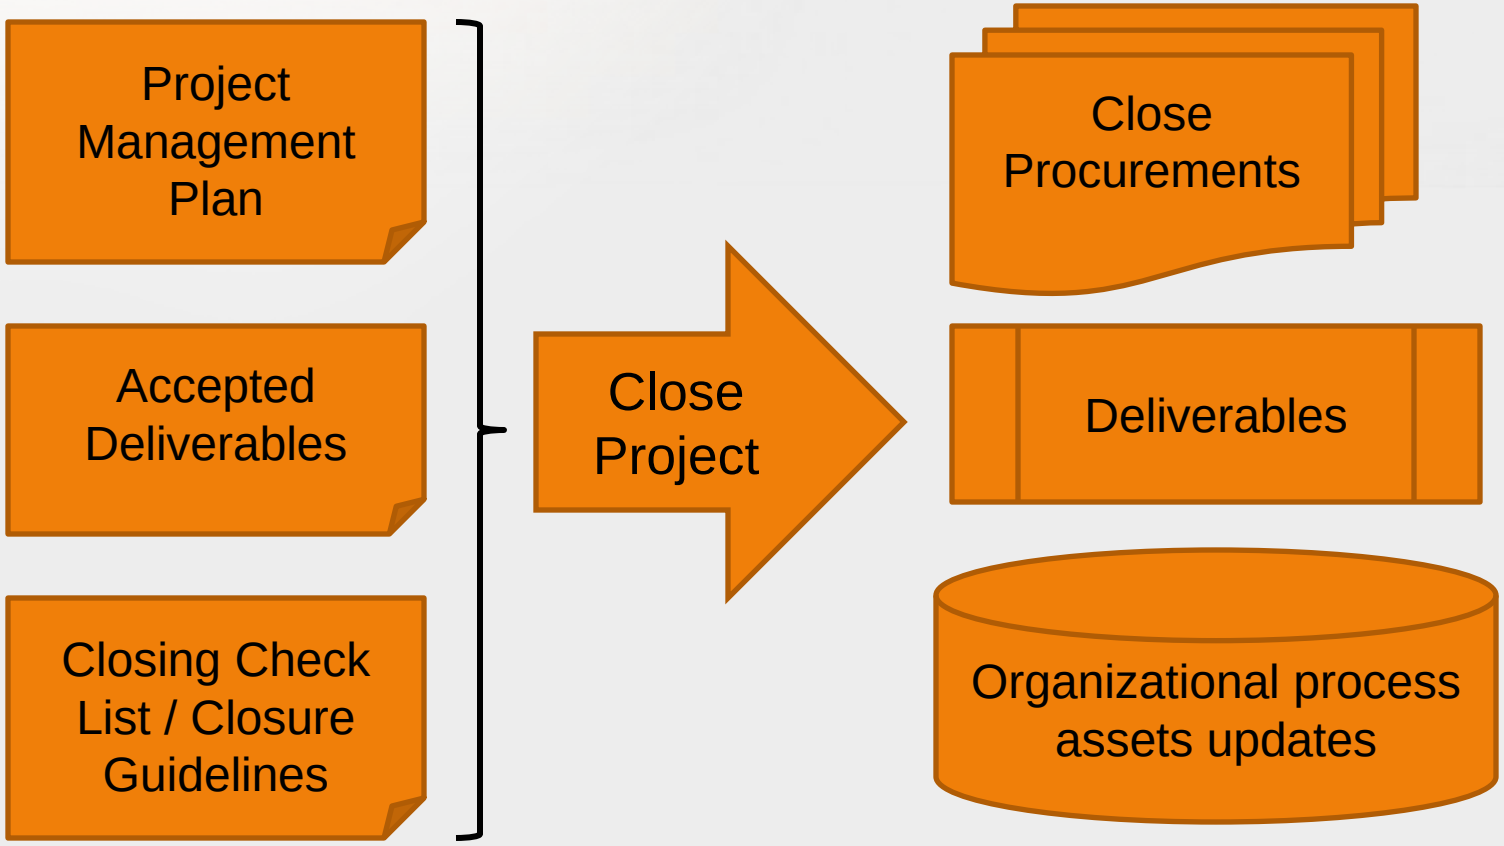

Close the Project Resources



Your Management



Suppliers



Product Safety



Client:

- Project Manager
- Sponsor
- Team members



Purchasing



Project Manager



Project Team



Engagement Manager




Pricer



System Architect



Project Assurance

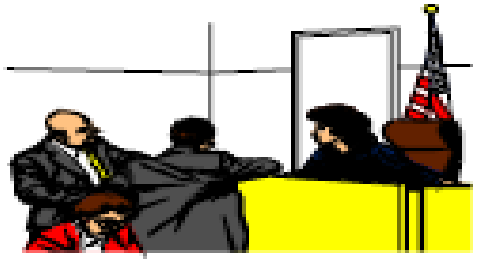

Legal

Project Completion Workshops

- One for the team
- One for the client
- Purposes:
  - Confirm that all deliverables were received
  - Recognize the contribution made by individuals
  - Publicize the success of the project
  - Ensure that experience gained and lessons learned from the project are incorporated into your organization's standards
- Mark and record the formal end of the project
- Measure and record project objectives:
  - Function
  - Quality
  - Performance
  - Cost
  - Schedule
  - Identifying end-of-project housekeeping activities
  - Lessons learned

Lessons Learned

- Lessons Learned - the learning gained from the process of performing the project. Lessons learned may be identified at any point

- **Timely**
- **Relevant**
- **In context**
- **Detailed**
- **Intellectual capital**



Project managers have a professional obligation to conduct lessons learned sessions for all projects

Assess the project

- Make project final report for your organization.
- Final report should be the document for lesson learned.
  - Good report point out the problems in process which are needed to be resolved for next other project.
  - Many stakeholders should be involved to write the report including PM, PMO, Sales manager etc.
- Final report includes assessment of each processes and their actual performance.

Give the feedback to project members

- One of the effective way to improve the motivation of project members for next project is giving feedback to them at the end of the project.
- Feedback need to include some point as follows:
  - Appreciation of his/her contribution
  - His/her strong point
  - His/her weak point which can be improved in future
- Remember to tell everyone that you have finished!
- Progress information from completed work is a valuable source for estimating future projects of a similar nature. Make sure the final figures have been collated and made available for future reference.
- Having celebration party with your stakeholders!

Key Messages

- Closure is essential to ensure that:
  - Formal acceptance of the project is made by the Client/project sponsor
  - Various project records are completed
  - Completion criteria are met for the final revision and issuance of documentation
  - Essential project documentation is retained
  - Lessons-learned are documented
  - Warranty is transferred, where applicable
- Administrative Closure is a process and must be carefully planned, budgeted, and scheduled just like any other phase of the project life cycle
  - Include a project closure plan in the project control book
  - Involve the same group of people in the project closure as were involved in project startup, where possible
  - Project closure begins on day one of the project

Project Manager's Responsibilities

- Assess the terms of agreement and the completion of all commitments
- Release the technical environment
- Obtain sponsor feedback
- Assess the lessons learned
- Close out the sponsor agreement
- Submit the intellectual capital

2. Đánh giá dự án

Project reviews

- Project reviews are opportunities to see the forest rather than the trees.
- Project reviews are not inquisitions, but opportunities to identify problems, escalate issues, and elicit management support when needed.

- The main tasks are to:
  - Review progress and achievements to date
  - Review plans and authorize the project to proceed to the next Project Management Review
  - Confirm the continued viability of the project
  - Review project control and assurance activities and reports
  - Review risks and issues making decisions and communicating results

Reviews should be conducted by an independent group of skilled reviewers outside of the project who can view the project objectively

Types of Project Management Reviews (based on the review time)

- Contract readiness review: within 2-8 weeks after the contract signing
- Periodic review : every 3-6 months
- Completion review: completed at the end of the project
- Special review: when a serious problem is appeared or when the project manager has reason to request one
- Compliance review: conducted by an organization, external to the project, by the sponsor, or by an outside body
  - Ensure that policies and procedures are being followed by the project
  - identify improvements that can be made to procedures.
- Business reviews: focuses on financial and business exposures

Neglect always carries a high cost, Project Reviews should be mandatory

Types of Project Management Reviews

- Deliverable review: before the deliverable or key component is released to the sponsor
  - ensure that no open items remain and that delivery is appropriate
- Project management reviews: focuses on the planning and control aspects of the project
- Technical reviews: focus on the technical aspects of the project:
  - Work products, deliverables, and subcontractor reviews
  - Traceability of requirements, architecture, and technology competitiveness

As the project manager, you must not rely totally on prescribed reviews but should exercise judgment in determining which reviews are necessary and when they should be held to make the project a success

Review topics

- Prior to the review, you should make arrangements with the review team leader to set the schedule for the review
- Typical activities to plan for a smooth review include:
  - The project manager's presentation
  - Interviews with key project members (including subcontractors)
  - Interviews with key customer project team members and project sponsor
  - Project documentation analysis
  - Review debrief with the project manager
- In the typical project management review, you have an opportunity to present your view of the project at the beginning of the review

Include project review activities in the project management plan

Review topics

- Project overview
  - project scope, objectives, major milestones, customer organization, project staffing (including subcontractors), and planning baselines.
- Highlight project accomplishments
  - All the good things that are happening on your project
- Overview of the project management processes you are following
  - Plans created and used to track project and
  - what are tools and methodologies used on the project
- Identify project-related risks and problems
  - Risks and problems with the actions that you are taking to mitigate the risks and solve those problems
  - Results of any earlier reviews about project management , solution or deliverable
  - Status of their associated action plans
- Provide an objective assessment of the health of the project
  - How is the project going and objective

Following your presentation, the reviewers will want to see your plans and status reports and talk to the other members of your team

Key Questions To Answer

- The reviewers want to understand where you are today

→ Determine by using the earned value (EV) indicators

  → where you are relative to the budget and the schedule today

  → where you will be at the end of the project

- The following key questions help to determine the health of a project
  - Where should the project be?
  - How much has been done?
  - How much has it cost?
  - How much will it take to finish?
  - What will it cost when it is done?

Project Management Review Components

- Review project documentation, especially the Project Control Book(PCB)
- Review cost data
- Review schedule data
- Review risk plan
- Review change control log
- Interview selected team members and the client/project sponsor
- Analyze the information collected
- Prepare a report of findings and recommendations

Key Messages

- The main purpose of a project management review is to provide general guidance to you as the project manager with an objective assessment of a project's health
- Reviews should be conducted by an independent group of skilled reviewers outside of the project who can view the project objectively
- Include project review activities in the project management plan
- Project management reviews are a great opportunity to:
  - Show your peers what you are doing, to learn something, and to get some help where you need it
  - Get some support to help you solve problems you might have that cannot be solved any other way
- Preparing for the project management review takes time
  - All of that work needs to be done anyway, and the project review just forces it to be done sooner
